Project Task Report

Linkere

Date Range: Feb 18, 2026 – Mar 18, 2026
Generated: March 18, 2026

Prepared by: Project Analytics System

1. Executive Summary

This report covers **148** tasks created between **February 18, 2026** and **March 18, 2026** for the **Linkere** project.

Metric	Value
Total Tasks Analysed	148
Overall Completion Rate	87.8%
Completed Tasks	130
In Progress Tasks	3
Pending Tasks	15
Bug Tasks (Yara Mahmoud)	0
Regular Tasks (Ahmed Abdelfattah)	8
Tasks with No Deadline	39
Overdue Tasks	3
Avg Days to Complete	2.8 days

2. Status Breakdown

Status	Count	Percentage
Completed	130	87.8%
In Progress	3	2.0%
Pending	15	10.1%

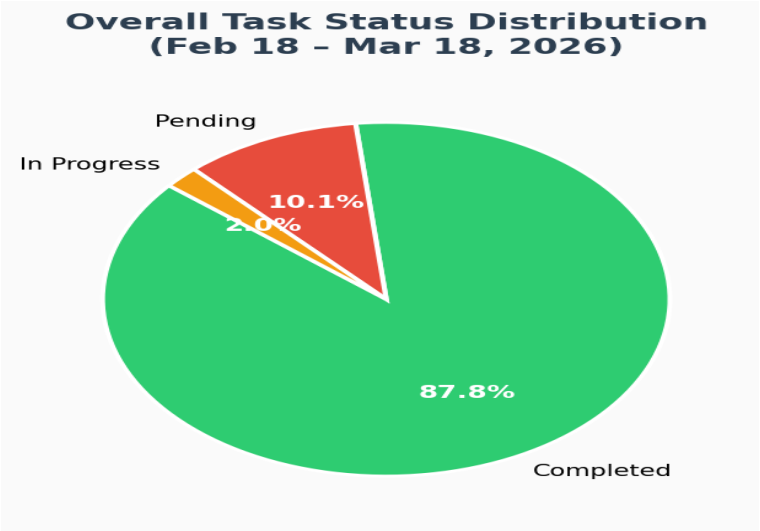

3. Assignee Performance

Assignee	Total	Completed	In Progress	Pending	Completion %
Ahmad Maghrapy	19	19	0	0	100.0%
Ahmed Abdelfattah	8	2	0	6	25.0%
Anwar Abdelmaksoud	40	35	0	5	87.5%
Hesham Raafat	1	0	0	1	0.0%
Mahmoud Abdelhamid	15	15	0	0	100.0%
Mohamed Salah	36	33	2	1	91.7%
Omar Adly	11	9	0	2	81.8%
ammar elkhouly	18	17	1	0	94.4%

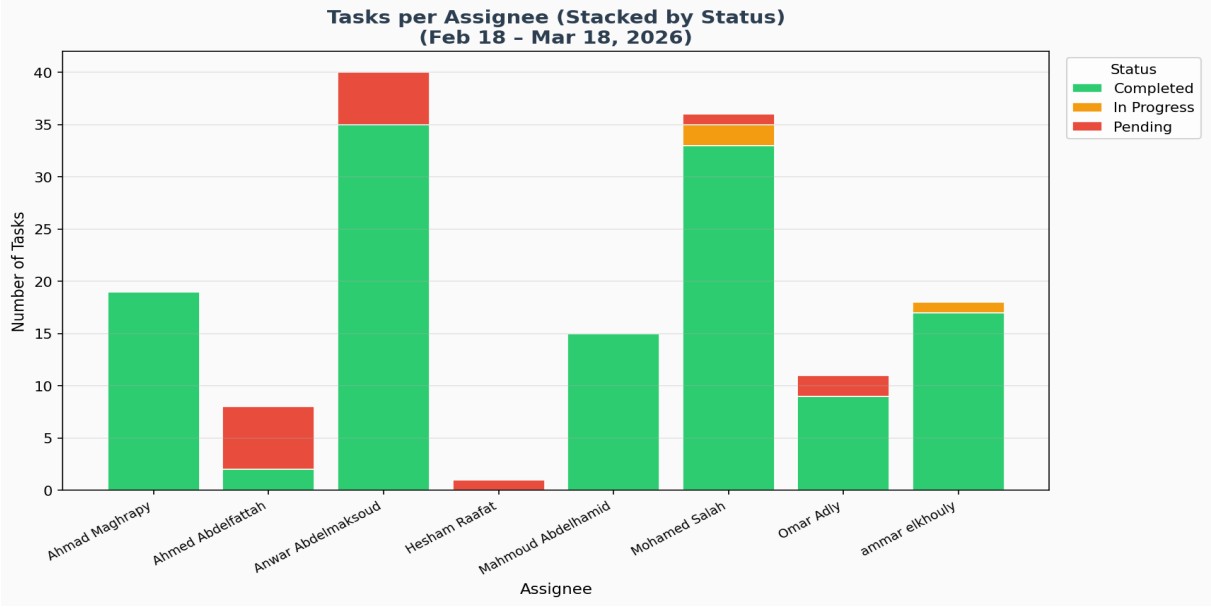

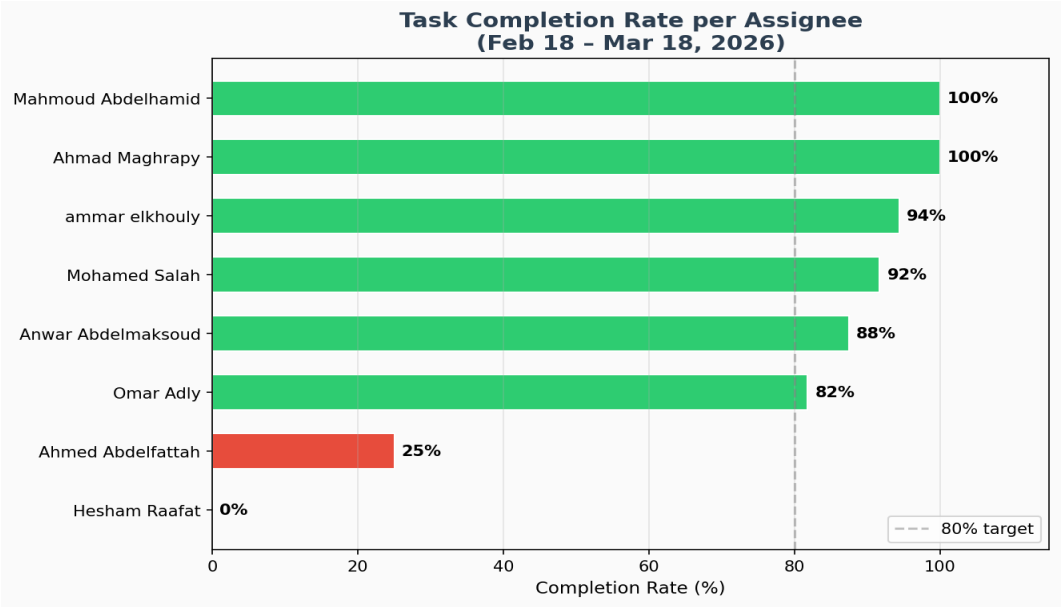
Task Completion Rate per Assignee
(Feb 18 – Mar 18, 2026)
Mahmoud Abdelhamid
Ahmad Maghrapy
ammar elkhouly
Mohamed Salah
Anwar Abdelmaksoud
Omar Adly
Ahmed Abdelfattah
Hesham Raafat
100%
100%
94%
92%
88%
82%
25%
0%
80% target
0
20
40
60
80
100
Completion Rate (%)

4. Bug Tasks — Yara Mahmoud

Task Name	Status	Created On	Deadline

5. Regular Tasks — Ahmed Abdelfattah

Task Name	Status	Created On	Deadline
[Linker Responsive - Website "Merchant" Module] Ma...	Pending	25 Feb 2026	—
User Story: Ex-Works (EXW) Checkout	Pending	26 Feb 2026	—
[Supplier View] Company profile update to collapse	Pending	01 Mar 2026	29 Mar 2026
[Admin-2] user story Admin Control over Merchant a...	Pending	01 Mar 2026	11 Mar 2026
[Admin-2] user story Admin Control over Merchant a...	Pending	01 Mar 2026	29 Mar 2026
Supplier Block	Completed	01 Mar 2026	11 Mar 2026
[Merchant-1] User Story – EXW Checkout	Completed	03 Mar 2026	09 Mar 2026
[Supplier-1] user story Add New Product	Pending	05 Mar 2026	12 Mar 2026

6. Visualisations

Category Breakdown

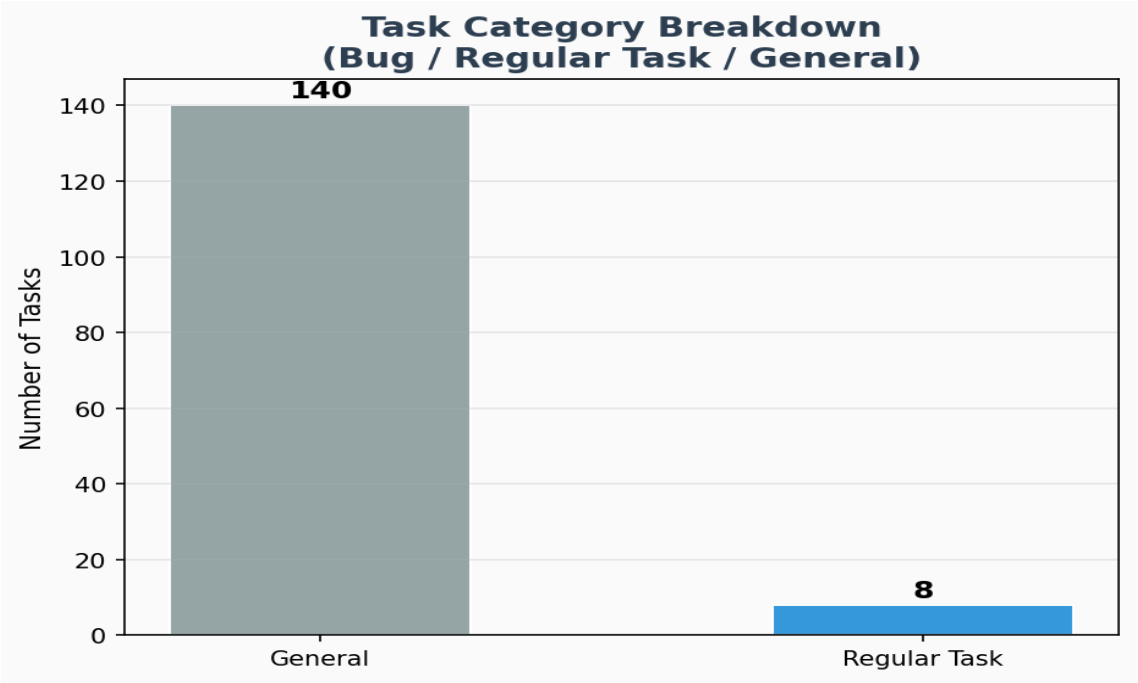

Tasks Created per Week

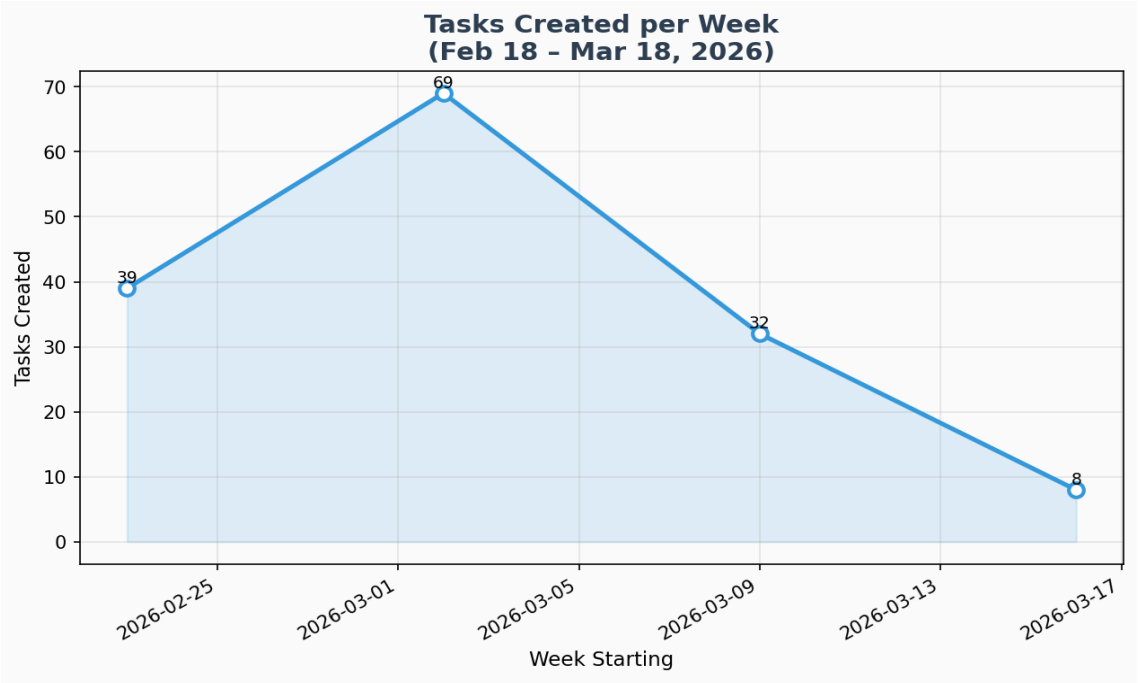

Assignee × Status Heatmap

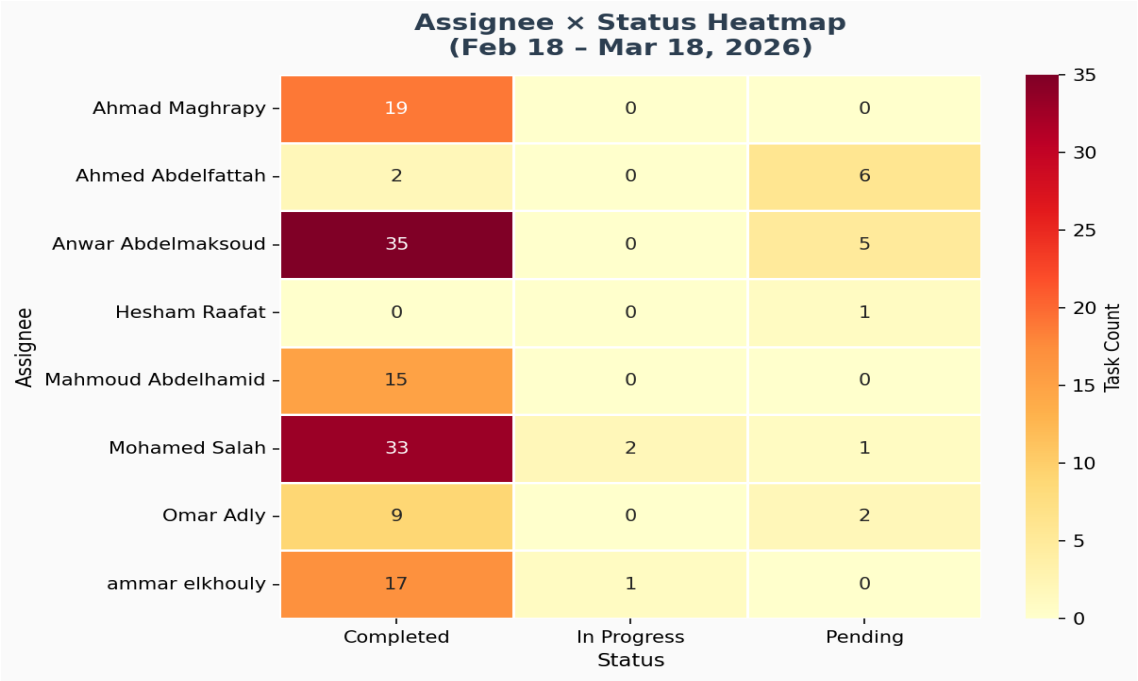

Completed Tasks per Week

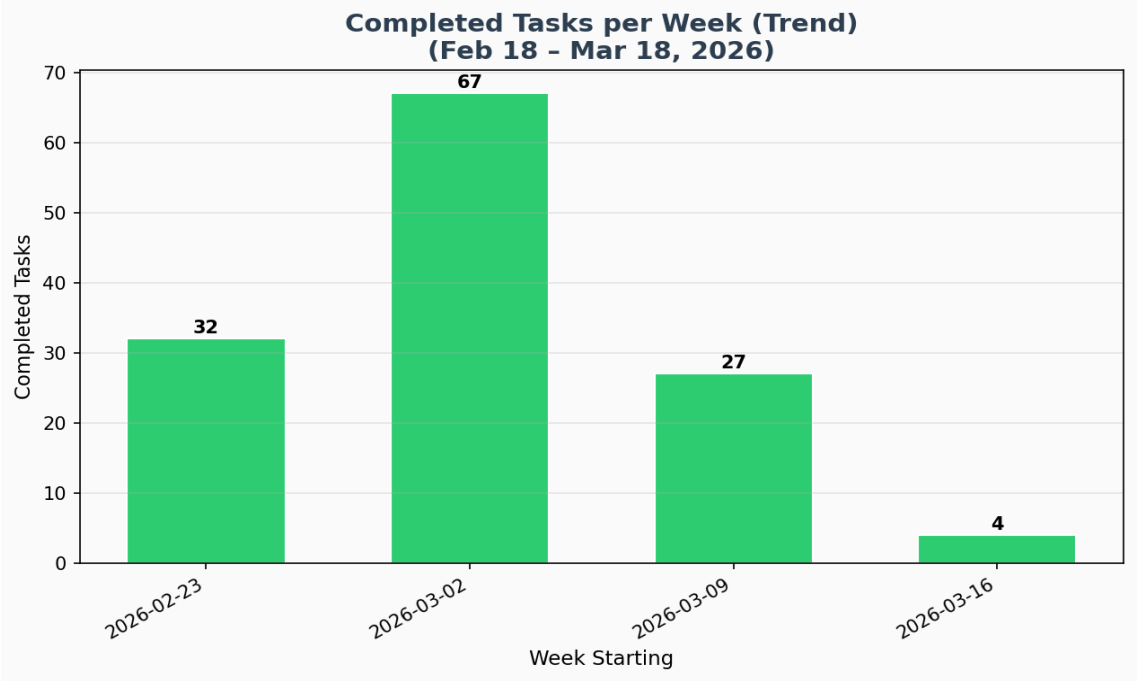

7. Key Insights & Recommendations

• **High Overall Completion:** The team achieved a **87.8%** completion rate across 148 tasks — indicating strong delivery in the Feb 18 – Mar 18 period.

• **Top Performer: Ahmad Maghrapy** leads with a **100%** completion rate, demonstrating consistent task throughput.

• **Needs Attention: Hesham Raafat** has the lowest completion rate at **0%**. A workload review or additional support may be beneficial.

• **Pending Backlog:** There are **15** pending tasks still open. Prioritising these in the next sprint will prevent accumulation.

• **Bug Tracking (Yara Mahmoud): 0** tasks are categorised as bugs. A dedicated bug-bash session is recommended if completion rate is below 80%.

• **Deadline Coverage: 39** tasks have no deadline assigned. Setting deadlines will improve sprint planning and accountability.

• **Average Cycle Time:** Completed tasks took an average of **2.8 days** from creation to completion — a useful baseline for future estimation.
